



# **SAN PEDRO CREEK**

Improvements Project

# PROJECT UPDATES

- Commissioners Court
- CMAR Contract
- Inlet to Dolorosa Action Plan
  - USACE Permit
  - Utility Relocation Coordination
  - Design Deliverables
  - ROW deliverables
- Construction Activities



# Commissioners Court

- Work Session September 27
  - Updated Budget Numbers
  - Funding Strategy
  - Recommended motion for funding for work packages
- Court Actions
  - Authorization of \$30 million for construction
  - Authorization of use of ADT and USACE reimbursement funds for San Pedro Creek
- October 18 Session
  - Recommendation for approval of construction phase services and Amendment of Construction ILA

# CMAR Contract

- Deliverable dates agreed upon
- Contract language being finalized
  - Project duration extension
  - Additional preconstruction phase services
  - Recovery Plan
  - Fee at Risk
- Subcontractor Agreements



# PHASE ONE SEGMENTS



# Action Plan Deliverables

- USACE Permit
  - Multiple meetings with USACE in Fort Worth conducted.
  - 404 & 408 timelines now meet plan requirements
  - Section 106 review duration being evaluated
  - Environmental Assessment submittal October 13

# Action Plan Deliverables

- Utility Relocation Coordination
  - Weekly coordination meetings ongoing
  - Joint Bore Cost Sharing
  - Close communication and coordination during construction

# Action Plan Deliverables

- Design Deliverables
  - Tunnel Inlet to Houston – 10 work packages (WP)
  - WP 1: Horizontal Directional Drills
    - Bids received
    - Construction to begin December 2016
  - WP2: Inlet to Houston Street Bridge
    - Excludes landscaping and wayfinding
    - Broken into smaller packages



# Action Plan Deliverables


- Design Deliverables
  - WP 3: Underpinning design
    - Commerce to Dolorosa
    - Submitted September 28
  - WP 4: Utilities & Demolition
    - Houston to Commerce
    - Submitted October 4
  - WP5: Structural Elements
    - Houston to Commerce
    - Due October 31

# Action Plan Deliverables

- ROW Deliverables
  - Acquisition of one parcel required
  - Temporary Construction Easements (TCEs)
    - COSA
      - Approved by Planning Commission
      - November 3<sup>rd</sup> City Council agenda
    - Ongoing coordination with private landowners

# Construction Activities

- Work Package 1
  - Start construction mid-December
  - Outreach to affected businesses ongoing
- Coordination with COSA TCI/CCDO
  - Traffic control planning
  - Parking solution
  - Construction Staging Area and Offices
- Coordination with other planned construction projects

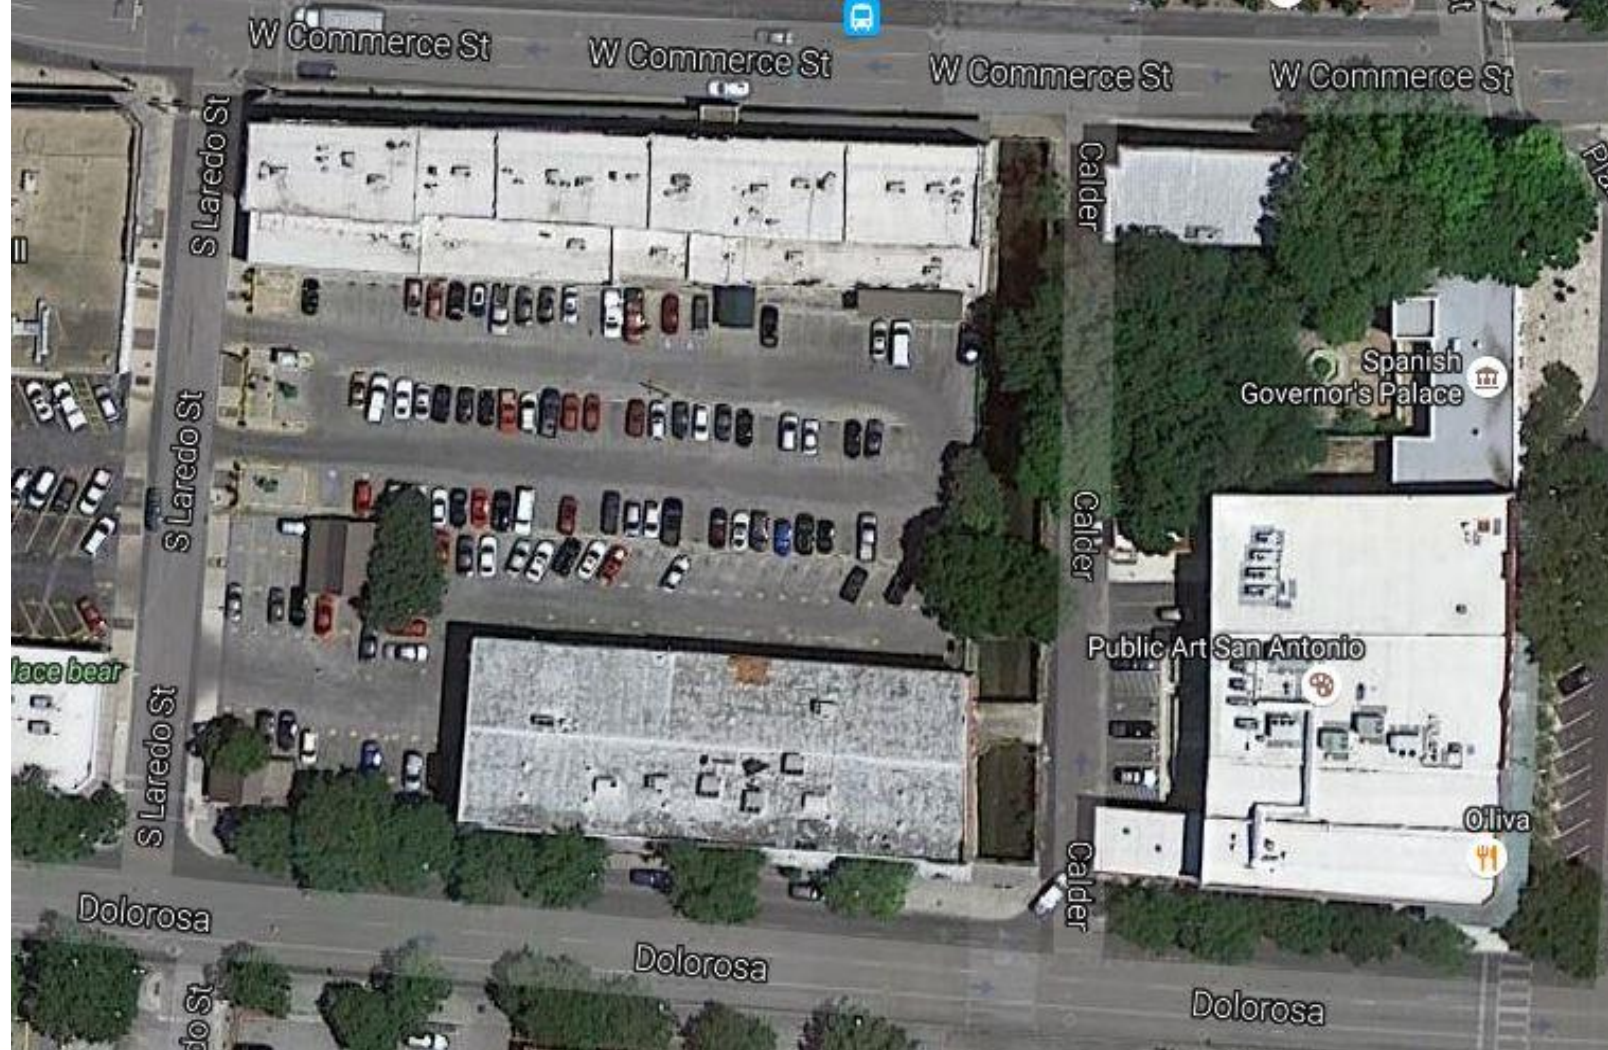



**san pedro creek**  
**improvements project**  
CONNECTING COMMUNITIES  
[WWW.SPCPROJECT.ORG](http://WWW.SPCPROJECT.ORG)

# Westside Creeks



City of San Antonio



## Linear Creekway Trails Project and Elmendorf Lake Park

Jeff Tyler

October 18, 2016

# Westside Creeks Linear Creekway Trails – Status Report


- Apache / San Pedro Hike and Bike Trails
  - 10' wide hike and bike linear creekway trails.
    - Apache 1.49 miles
    - San Pedro 2.01 miles
  - Apache Creek North (Cassiano Park to San Pedro) Grand Opening held July 9th, 2016
  - Apache Creek South (19<sup>th</sup> Street to Cassiano Park)
    - Construction Kickoff Oct. 2016 (18-month Duration)
    - Trail constructed as part of SAWS C-5 and C-28 Project
  - San Pedro Creek Grand Opening held August 20th , 2016
  - Project Progress Page
    - <http://www.westsidecreeks.com/apachesan-pedro-creekways-trail-progress/>
- Alazan / Martinez Hike and Bike Trails
  - 10' wide hike and bike linear creekway trails.
    - Alazán 0.47 miles
    - Martinez 0.61 miles
  - Grand Opening held June 18, 2016
  - Project Progress Pages
    - <http://www.westsidecreeks.com/alazan-creekway-trail-progress/>
    - <http://www.westsidecreeks.com/martinez-creekway-trail-progress/>



# Trail Projects (Sales Tax Initiative)

## 2016 Design Solicitation Details


- Released October 2016 Due November 2016
- Selections December 2016
- Execute Contracts January 2016
- Includes Martinez Creek, Alazan Creek, San Pedro Creek, and Zarzamora Creek.
- Advertised on the [www.sara-tx.org](http://www.sara-tx.org) website and in the Express News
- Letter from St. Mary's University President Thomas Mengler, J.D.

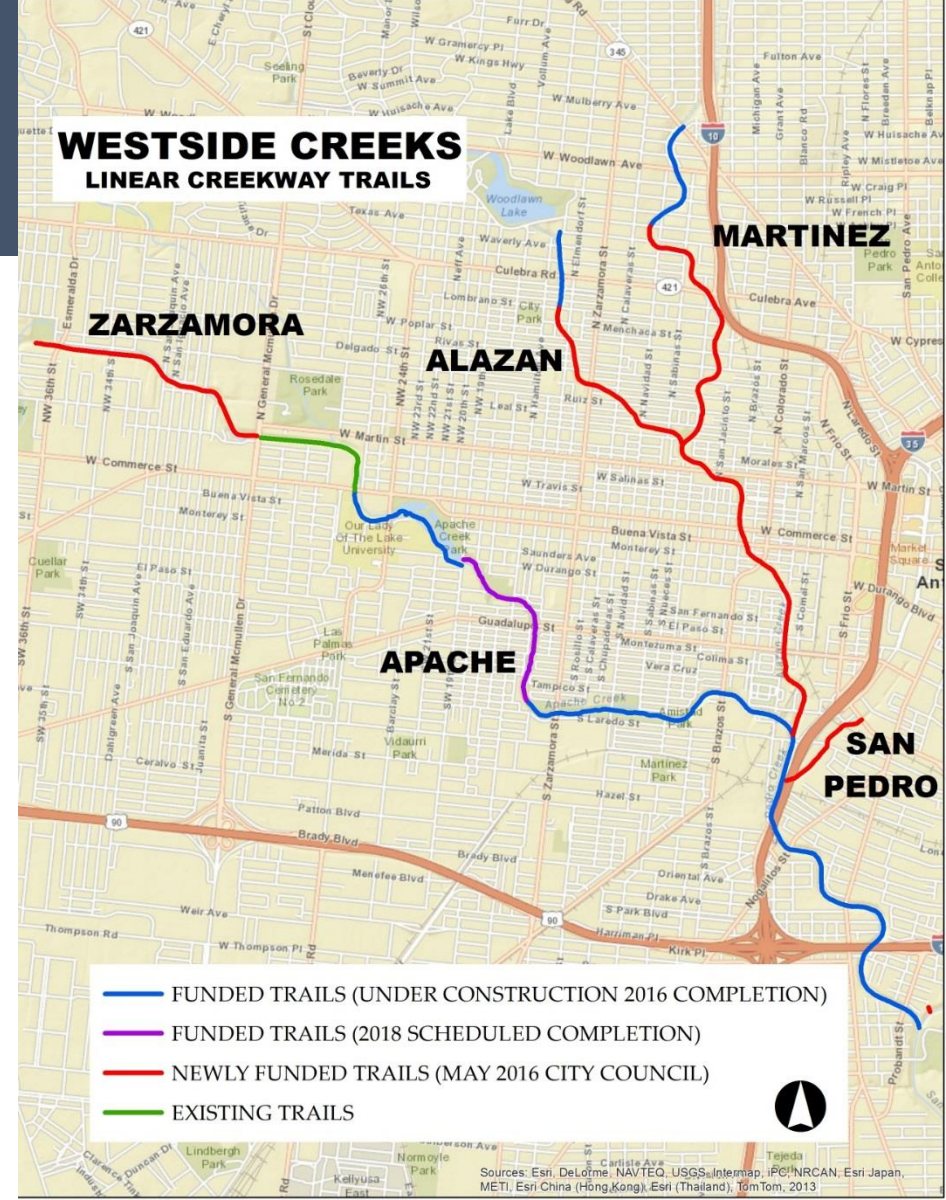



# Elmendorf Lake Park – Status Report

- Elmendorf Lake Park (Completion)
  - 1) Jerdon – Bridge Project (06/2016)
  - 2) MAC, Inc – South Project (07/2016)
  - 3) Journeyman – North Project (12/2016)
  - Project Progress Page
    - <http://www.westsidecreeks.com/elmendorflakeimprovementsprogress/>
    - Approximately 95% complete

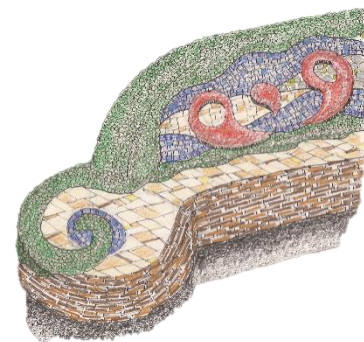

Approx. 90%  
Progress to Date

Substantially Complete

COMMERCE

SW 24TH

NW 20

NW 20

NW 19TH

BUENA VISTA


SHORE

MONTERE

OUR LADY OF THE LAKE UNIVERSITY

CESAR E. CHAVEZ

SAUNDERS

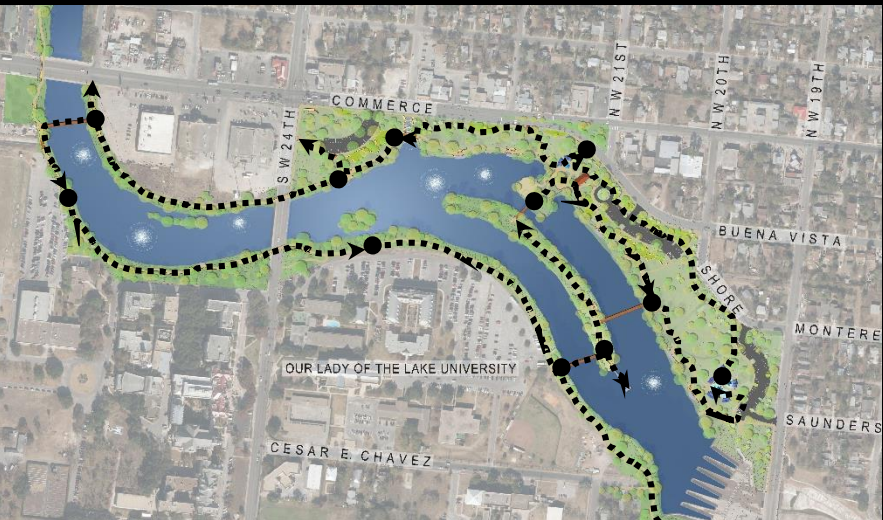

# Westside Creeks



City of San Antonio




## Trash and Floatables Collection System along Alazan Creek

October 18, 2016

# Trash and Floatables - Status Update

- Litter Trap with Trash Boom installation on Alazan Creek
- Upstream of El Paso and downstream of S. Colorado Street
- Installed October 2016
- Educational Programming currently being coordinated

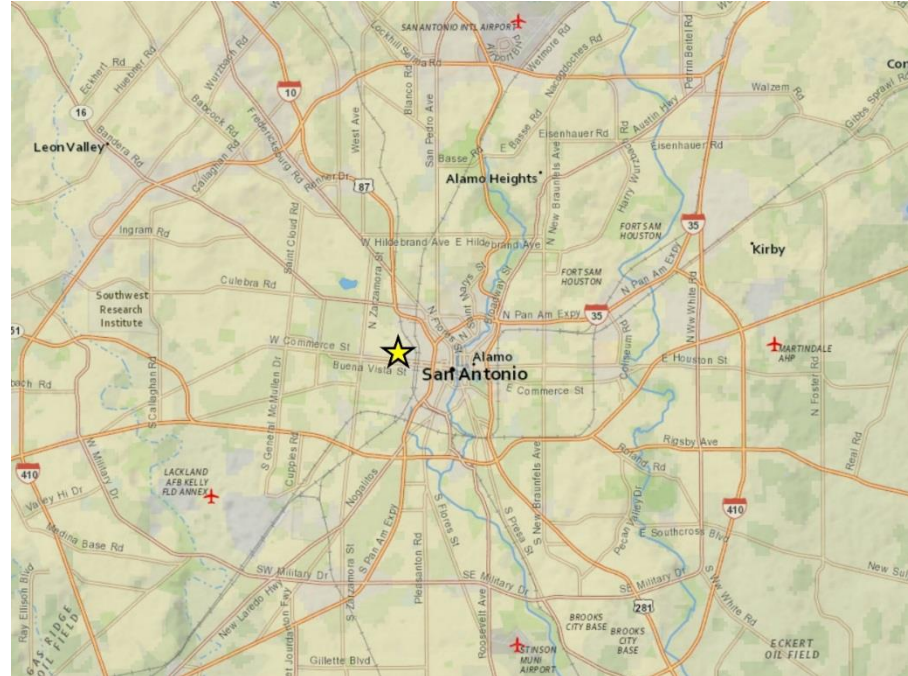

# Trash and Floatables - Status Update



Pre-Project



Post-Project

